




PROJECT INFORMATION	
PROJECT NAME: PARTNERSHIP 3 ROOM 120 ELECTRICAL MODIFICATION FOR ARCC	DATE COMPLETED: JANUARY 12, 2022
PROJECT NUMBER: 21812601	PROJECT MANAGER: SAMANTHA MASON
SQUARE FOOTAGE: NA	COST PER SQUARE FOOT: NA

PROJECT DESCRIPTION: REPLACE 3 PAIRS OF 30A CIRCUIT BREAKER PLUGS WITH 60A CIRCUIT BREAKER PLUGS IN ROOM 120 AT PARTNERSHIP 3. THE PROJECT SCHEDULE WAS DELAYED BY 9 MONTHS DUE TO SUPPLY CHAIN ISSUES WHICH DELAYED THE MANUFACTURE AND ARRIVAL OF A SPECIALIZED PART ONLY AVAILABLE FROM ONE MANUFACTURER.



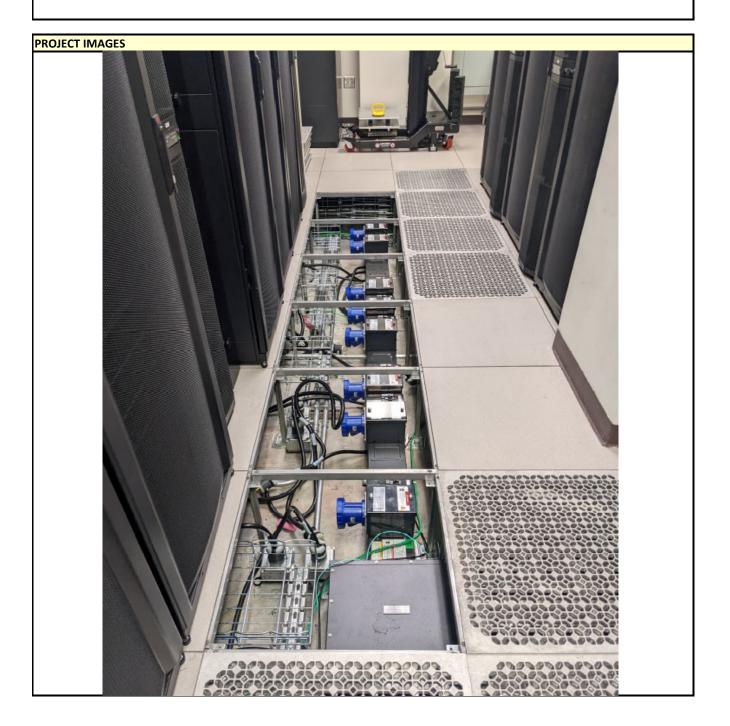



PROJECT INFORMATION	
PROJECT NAME: PARTNERSHIP 3 ROOM 120 ELECTRICAL MODIFICATION FOR ARCC	DATE COMPLETED: JANUARY 12, 2022
PROJECT NUMBER: 21812601	PROJECT MANAGER: SAMANTHA MASON
SQUARE FOOTAGE: NA	COST PER SQUARE FOOT: NA

PROJECT DESCRIPTION: REPLACE 3 PAIRS OF 30A CIRCUIT BREAKER PLUGS WITH 60A CIRCUIT BREAKER PLUGS IN ROOM 120 AT PARTNERSHIP 3. THE PROJECT SCHEDULE WAS DELAYED BY 9 MONTHS DUE TO SUPPLY CHAIN ISSUES WHICH DELAYED THE MANUFACTURE AND ARRIVAL OF A SPECIALIZED PART ONLY AVAILABLE FROM ONE MANUFACTURER.

PROJECT COST	
DESIGN COST	\$ -
ARCHITECT / ENGINEER / INTERIOR DESIGN	\$ -
CONSTRUCTION COST	\$ 24,440.00
DIVISION 1 - GENERAL REQUIREMENTS (DUMPSTERS, ETC.)	\$ -
DIVISION 2 - EXISTING CONDITIONS	\$ -
DIVISION 3 - CONCRETE	\$ -
DIVISION 4 - MASONRY	\$ -
DIVISION 5 - METALS	\$
DIVISION 6 - WOOD, PLASTICS & COMPOSITES	\$
DIVISION 7 - THERMAL & MOISTURE PROTECTION	\$ -
DIVISION 8 - OPENINGS	\$ -
DIVISION 9 - FINISHES	\$ -
DIVISION 10 - SPECIALTIES	\$ -
DIVISION 11 - EQUIPMENT	\$ -
DIVISION 12 - FURNISHINGS	\$ -
DIVISION 13 - SPECIAL CONSTRUCTION	\$ -
DIVISION 14 - CONVEYING EQUIPMENT	\$ -
DIVISION 21 - FIRE SUPRESSION	\$ -
DIVISION 22 - PLUMBING	\$ -
DIVISION 23 - HVAC	\$ -
DIVISION 26 - ELECTRICAL	\$ 24,440.00
DIVISION 27 - COMMUNICATIONS	\$ -
DIVISION 28 - ELECTRONIC SAFETY & SECURITY	\$ -
DIVISION 31 - EARTHWORK	\$ -
DIVISION 32 - EXTERIOR IMPROVEMENT	\$ -
DIVISION 33 - UTILITIES	\$ -
COMMISSIONING	\$
GENERAL LIABILITY	\$
GENERAL CONDITIONS (STAFFING, ETC.)	\$
CONTRACTOR'S FEE (OVERHEAD & PROFIT)	\$
PAYMENT & PERFORMANCE BOND (NOT REQ'D IF UNDER \$100K)	\$ -
INFORMATION TECHNOLOGIES & RESOURCES COST	\$ -
UCF IT	\$
OFFICE OF INSTRUCTIONAL RESOURCES (OIR)	\$ -
FACILITIES & SAFETY COST	\$ 1,316.52
BUILDING CODE OFFICE	\$ 510.00
STATE FIRE MARSHALL	\$ -
FP&C PROFESSIONAL MANAGEMENT SERVICES	\$ 806.52
FACILITIES OPERATIONS ALLOWANCE	\$ -
CONSTRUCTION CONTINGENCY (10%, REFUNDED IF NOT USED)	\$ -
TOTAL PROJECT COST	\$ 25,756.52

PROJECT SUBMITTED BY CLIENT SPAA, F&S REVIEW PM ASSIGNED PM CONTACTS REQUESTER PM DEVELOPS SCOPE A/E SELECTED A/E PROPOSAL REVIEW MPP TO CLIENT CLIENT APPROVAL AND FUNDING REQUISITION GENERATED PO ISSUED (NOTICE TO PROCEED) A/E DESIGN WORKSHOPS PERMIT REVIEWS	1.25 MONTHS
PM ASSIGNED PM CONTACTS REQUESTER PM DEVELOPS SCOPE A/E SELECTED A/E PROPOSAL REVIEW MPP TO CLIENT CLIENT APPROVAL AND FUNDING REQUISITION GENERATED PO ISSUED (NOTICE TO PROCEED) A/E DESIGN WORKSHOPS PERMIT REVIEWS	
PM CONTACTS REQUESTER PM DEVELOPS SCOPE A/E SELECTED A/E PROPOSAL REVIEW MPP TO CLIENT CLIENT APPROVAL AND FUNDING REQUISITION GENERATED PO ISSUED (NOTICE TO PROCEED) A/E DESIGN WORKSHOPS PERMIT REVIEWS	
PM DEVELOPS SCOPE A/E SELECTED A/E PROPOSAL REVIEW MPP TO CLIENT CLIENT APPROVAL AND FUNDING REQUISITION GENERATED PO ISSUED (NOTICE TO PROCEED) A/E DESIGN WORKSHOPS PERMIT REVIEWS	NA
A/E SELECTED A/E PROPOSAL REVIEW MPP TO CLIENT CLIENT APPROVAL AND FUNDING REQUISITION GENERATED PO ISSUED (NOTICE TO PROCEED) A/E DESIGN WORKSHOPS PERMIT REVIEWS	NA
A/E PROPOSAL REVIEW MPP TO CLIENT CLIENT APPROVAL AND FUNDING REQUISITION GENERATED PO ISSUED (NOTICE TO PROCEED) A/E DESIGN WORKSHOPS PERMIT REVIEWS	NA
MPP TO CLIENT CLIENT APPROVAL AND FUNDING REQUISITION GENERATED PO ISSUED (NOTICE TO PROCEED) A/E DESIGN WORKSHOPS PERMIT REVIEWS	NA
CLIENT APPROVAL AND FUNDING REQUISITION GENERATED PO ISSUED (NOTICE TO PROCEED) A/E DESIGN WORKSHOPS PERMIT REVIEWS	NA
REQUISITION GENERATED PO ISSUED (NOTICE TO PROCEED) A/E DESIGN WORKSHOPS PERMIT REVIEWS	NA
PO ISSUED (NOTICE TO PROCEED) A/E DESIGN WORKSHOPS PERMIT REVIEWS	NA
A/E DESIGN WORKSHOPS PERMIT REVIEWS	
WORKSHOPS PERMIT REVIEWS	
PERMIT REVIEWS	
S/S PERMIT DRAWINGS RECV'D	
PERMIT SUBMISSION	
BUILDING CODE OFFICE REVIEW	
STATE FIRE MARSHALL REVIEW	
CONTRACTOR WALK-THROUGH	
CONTRACTOR BID	7.75 MONTHS
PM REVIEWS BID	
AVP F&S APPROVAL OF BID	
PM PREPARES MPP	
MPP TO CLIENT	
CLIENT APPROVAL AND FUNDING	
REQUISITION GENERATED	
PO ISSUED (NOTICE TO PROCEED)	
CONSTRUCTION STARTS	
RFIS, SUBMITTALS, DOCUMENTS	
PROGRESS REVIEWS	
PAYMENT APPLICATIONS, INVOICES	2 E MONTUS
INSPECTIONS	3.5 MONTHS
CERTIFICATE OF COMPLETION	
CERTIFICATE OF OCCUPANCY	
BENEFICIAL OCCUPANCY BY CLIENT	
PUNCH LIST COMPLETION	
FINAL INVOICES	
OWNER'S MANUALS	1 MONTH
ASSET TURNOVER TO OPERATIONS	
ACCOUNTING CLOSE-OUT	
	E/S PERMIT DRAWINGS RECV'D PERMIT SUBMISSION BUILDING CODE OFFICE REVIEW STATE FIRE MARSHALL REVIEW CONTRACTOR WALK-THROUGH CONTRACTOR BID PM REVIEWS BID AVP F&S APPROVAL OF BID PM PREPARES MPP MPP TO CLIENT CLIENT APPROVAL AND FUNDING REQUISITION GENERATED PO ISSUED (NOTICE TO PROCEED) CONSTRUCTION STARTS REIS, SUBMITTALS, DOCUMENTS PROGRESS REVIEWS PAYMENT APPLICATIONS, INVOICES INSPECTIONS CERTIFICATE OF COMPLETION CERTIFICATE OF COUPANCY BENEFICIAL OCCUPANCY PUNCH LIST COMPLETION FINAL INVOICES OWNER'S MANUALS ASSET TURNOVER TO OPERATIONS
