




PROJECT INFORMATION	
PROJECT NAME: PHYSICAL SCIENCES ROOM 249 POWER & VENTILATION FOR INSTRUMENTS	DATE COMPLETED: OCTOBER 26, 2022
PROJECT NUMBER: 22121001	PROJECT MANAGER: JASON MOTTO
PROJECT DESCRIPTION: INSTALLATION OF 208V CEILING OUTLET FOR NEW LAB EQUIPMENT IN ROOM 249 AT PHYSICAL SCIENCES. PROJECT REQUIRED ELECTRICAL DESIGN BY AN A/E. EXISTING SNORKEL VENTILATION WAS EXTENDED TO PROVIDE VENTILATION FOR EXISTING EQUIPMENT.	



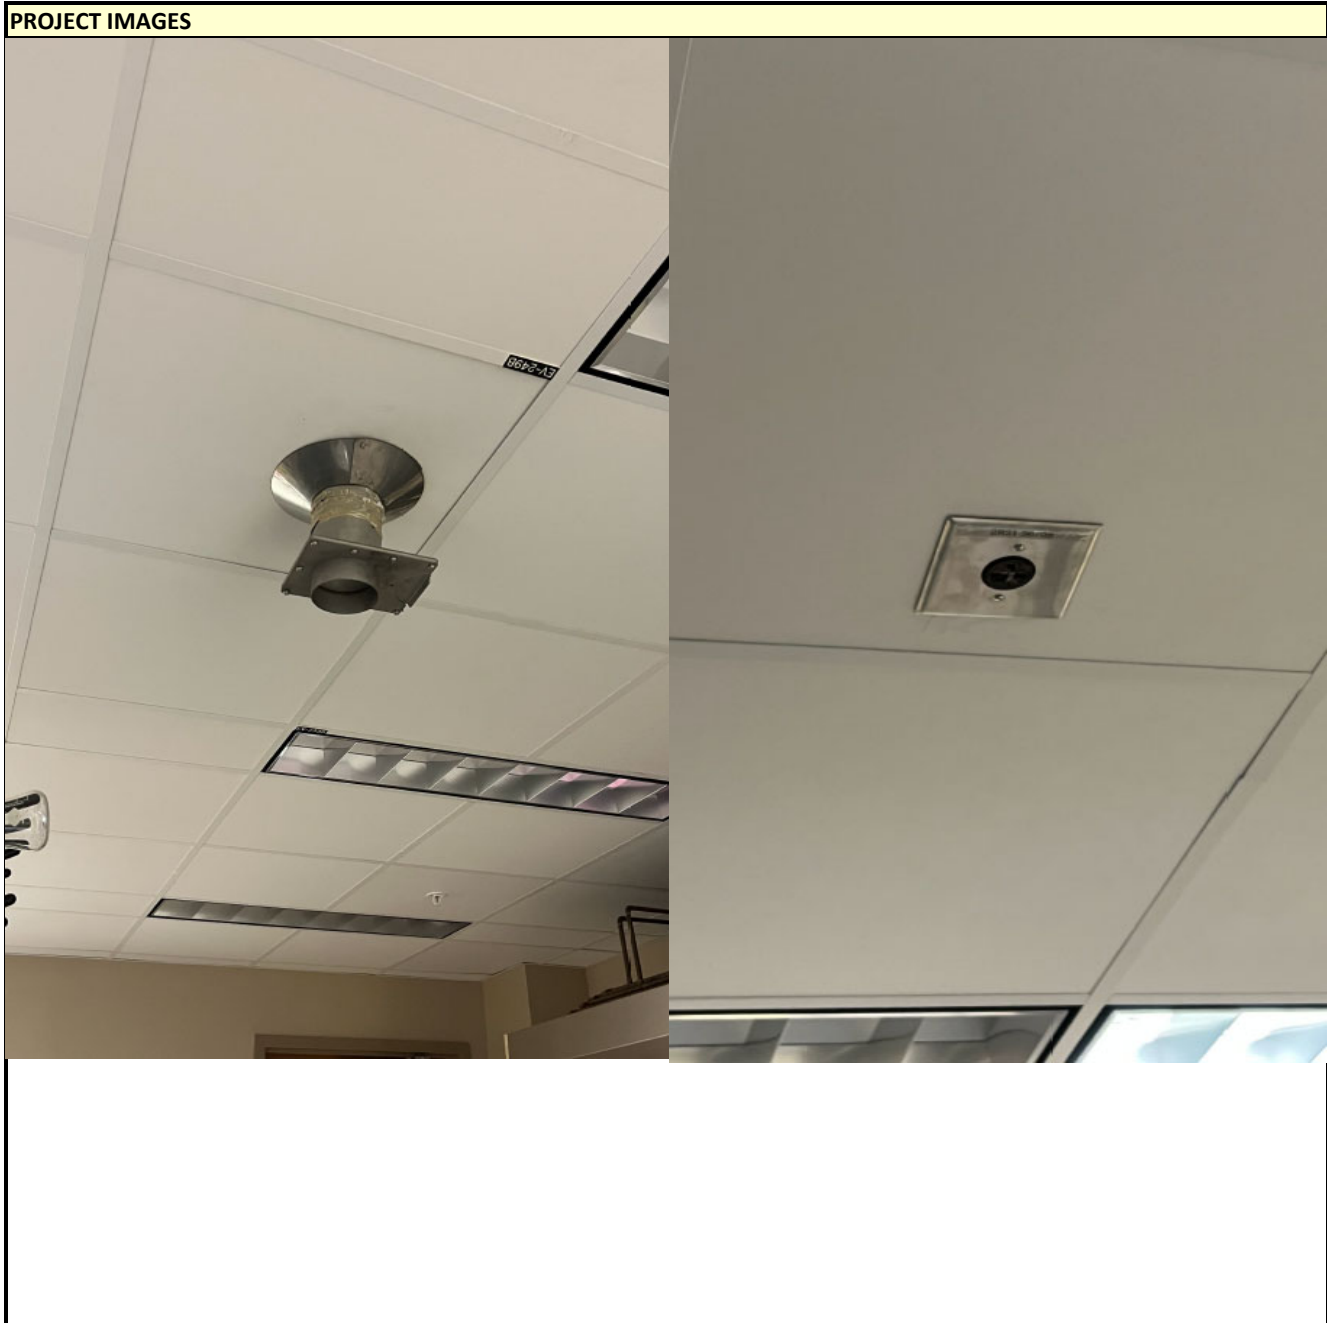

PROJECT INFORMATION	
PROJECT NAME: PHYSICAL SCIENCES ROOM 249 POWER & VENTILATION FOR INSTRUMENTS	DATE COMPLETED: OCTOBER 26, 2022
PROJECT NUMBER: 22121001	PROJECT MANAGER: JASON MOTTO
PROJECT DESCRIPTION: INSTALLATION OF 208V CEILING OUTLET FOR NEW LAB EQUIPMENT IN ROOM 249 AT PHYSICAL SCIENCES. PROJECT REQUIRED ELECTRICAL DESIGN BY AN A/E. EXISTING SNORKEL VENTILATION WAS EXTENDED TO PROVIDE VENTILATION FOR EXISTING EQUIPMENT.	

PROJECT COST	
<b>DESIGN COST</b>	<b>\$ 2,537.00</b>
ARCHITECT / ENGINEER / INTERIOR DESIGN	\$ 2,537.00
<b>CONSTRUCTION COST</b>	<b>\$ 12,958.00</b>
DIVISION 1 - GENERAL REQUIREMENTS (DUMPSTERS, ETC.)	\$ 1,893.00
DIVISION 2 - EXISTING CONDITIONS	\$ -
DIVISION 3 - CONCRETE	\$ -
DIVISION 4 - MASONRY	\$ -
DIVISION 5 - METALS	\$ -
DIVISION 6 - WOOD, PLASTICS & COMPOSITES	\$ -
DIVISION 7 - THERMAL & MOISTURE PROTECTION	\$ -
DIVISION 8 - OPENINGS	\$ -
DIVISION 9 - FINISHES	\$ -
DIVISION 10 - SPECIALTIES	\$ -
DIVISION 11 - EQUIPMENT	\$ -
DIVISION 12 - FURNISHINGS	\$ -
DIVISION 13 - SPECIAL CONSTRUCTION	\$ -
DIVISION 14 - CONVEYING EQUIPMENT	\$ -
DIVISION 21 - FIRE SUPPRESSION	\$ -
DIVISION 22 - PLUMBING	\$ -
DIVISION 23 - HVAC	\$ 5,100.00
DIVISION 26 - ELECTRICAL	\$ 1,900.00
DIVISION 27 - COMMUNICATIONS	\$ -
DIVISION 28 - ELECTRONIC SAFETY & SECURITY	\$ -
DIVISION 31 - EARTHWORK	\$ -
DIVISION 32 - EXTERIOR IMPROVEMENT	\$ -
DIVISION 33 - UTILITIES	\$ -
COMMISSIONING	\$ -
GENERAL LIABILITY	\$ -
GENERAL CONDITIONS (STAFFING, ETC.)	\$ 3,225.00
CONTRACTOR'S FEE (OVERHEAD & PROFIT)	\$ 840.00
PAYMENT & PERFORMANCE BOND (NOT REQ'D IF UNDER \$100K)	\$ -
<b>INFORMATION TECHNOLOGIES &amp; RESOURCES COST</b>	<b>\$ -</b>
UCF IT	\$ -
OFFICE OF INSTRUCTIONAL RESOURCES (OIR)	\$ -
<b>FACILITIES &amp; SAFETY COST</b>	<b>\$ 2,790.11</b>
BUILDING CODE OFFICE	\$ 318.00
STATE FIRE MARSHALL	\$ -
FP&C PROFESSIONAL MANAGEMENT SERVICES	\$ 2,472.11
FACILITIES OPERATIONS ALLOWANCE	\$ -
CONSTRUCTION CONTINGENCY (10%, REFUNDED IF NOT USED)	\$ -
<b>TOTAL PROJECT COST</b>	<b>\$ 18,285.11</b>

PROJECT TIME		
START	PROJECT SUBMITTED BY CLIENT	1.75 MONTHS
	SPAA, F&S REVIEW	
	PM ASSIGNED	
	PM CONTACTS REQUESTER	
DESIGN	PM DEVELOPS SCOPE	5.5 MONTHS
	A/E SELECTED	
	A/E PROPOSAL REVIEW	
	MPP TO CLIENT	
	CLIENT APPROVAL AND FUNDING	
	REQUISITION GENERATED	
	PO ISSUED (NOTICE TO PROCEED)	
	A/E DESIGN	
BID/PERMIT	WORKSHOPS	0.75 MONTHS
	PERMIT REVIEWS	
	S/S PERMIT DRAWINGS REC'D	
	PERMIT SUBMISSION	
	BUILDING CODE OFFICE REVIEW	
	STATE FIRE MARSHALL REVIEW	
	CONTRACTOR WALK-THROUGH	
	CONTRACTOR BID	
	PM REVIEWS BID	
	AVP F&S APPROVAL OF BID	
CONSTRUCTION	PM PREPARES MPP	2.5 MONTHS
	MPP TO CLIENT	
	CLIENT APPROVAL AND FUNDING	
	REQUISITION GENERATED	
	PO ISSUED (NOTICE TO PROCEED)	
	CONSTRUCTION STARTS	
	RFIS, SUBMITTALS, DOCUMENTS	
CLOSE-OUT	PROGRESS REVIEWS	3.75 MONTHS
	PAYMENT APPLICATIONS, INVOICES	
	INSPECTIONS	
	CERTIFICATE OF COMPLETION	
	CERTIFICATE OF OCCUPANCY	
	BENEFICIAL OCCUPANCY BY CLIENT	
TOTAL PROJECT TIME - 14.25 MONTHS	PUNCH LIST COMPLETION	3.75 MONTHS
	FINAL INVOICES	
	OWNER'S MANUALS	
	ASSET TURNOVER TO OPERATIONS	
ACCOUNTING CLOSE-OUT		
