




PROJECT INFORMATION	
PROJECT NAME: MATH SCIENCES ADD ACCESS CONTROL	DATE COMPLETED: JUNE 1, 2023
PROJECT NUMBER: 23012001	PROJECT MANAGER: SCOTT SUTO
NUMBER OF DOORS: 20	COST PER DOOR: \$8,200.34
PROJECT DESCRIPTION: ADDITION OF 20 DOORS OF ACCESS CONTROL AT THE MATH SCIENCES BUILDING. THE ENTRY DOORS TO ROOMS 108, 109, 121, 204, 260, 306, 336, 359, 360, 405, 406, AND 407 WERE RETROFITTED WITH DOOR CONTACTS, NEW ELECTRONIC MORTISE LOCKS OR LATCH RETRACTION KITS, ELECTRONIC TRANSFER HINGES, AND HID SIGNO CARD READERS. THE ALTERNATE ENTRY DOORS FOR ROOMS 121, 260, 306, 336, AND 406 WERE SETUP AS "TIME LOCK" DOORS AND RETROFITTED WITH DOOR CONTACTS, NEW ELECTRONIC MORTISE LOCKS OR LATCH RETRACTION KITS, AND ELECTRONIC TRANSFER HINGES. NEW LIFESAFETY POWER SUPPLY CABINETS ADDED IN TELECOM ROOMS 128, 222, 325, 353, AND 424. A NEW OPEN OPTIONS SSP CONTROLLER ADDED TO ROOM 128. OPEN OPTIONS RSC-2 SUB-CONTROLLERS ADDED TO THE EXISTING PANELS IN ROOMS 156 AND 246.	

**PROJECT IMAGES**



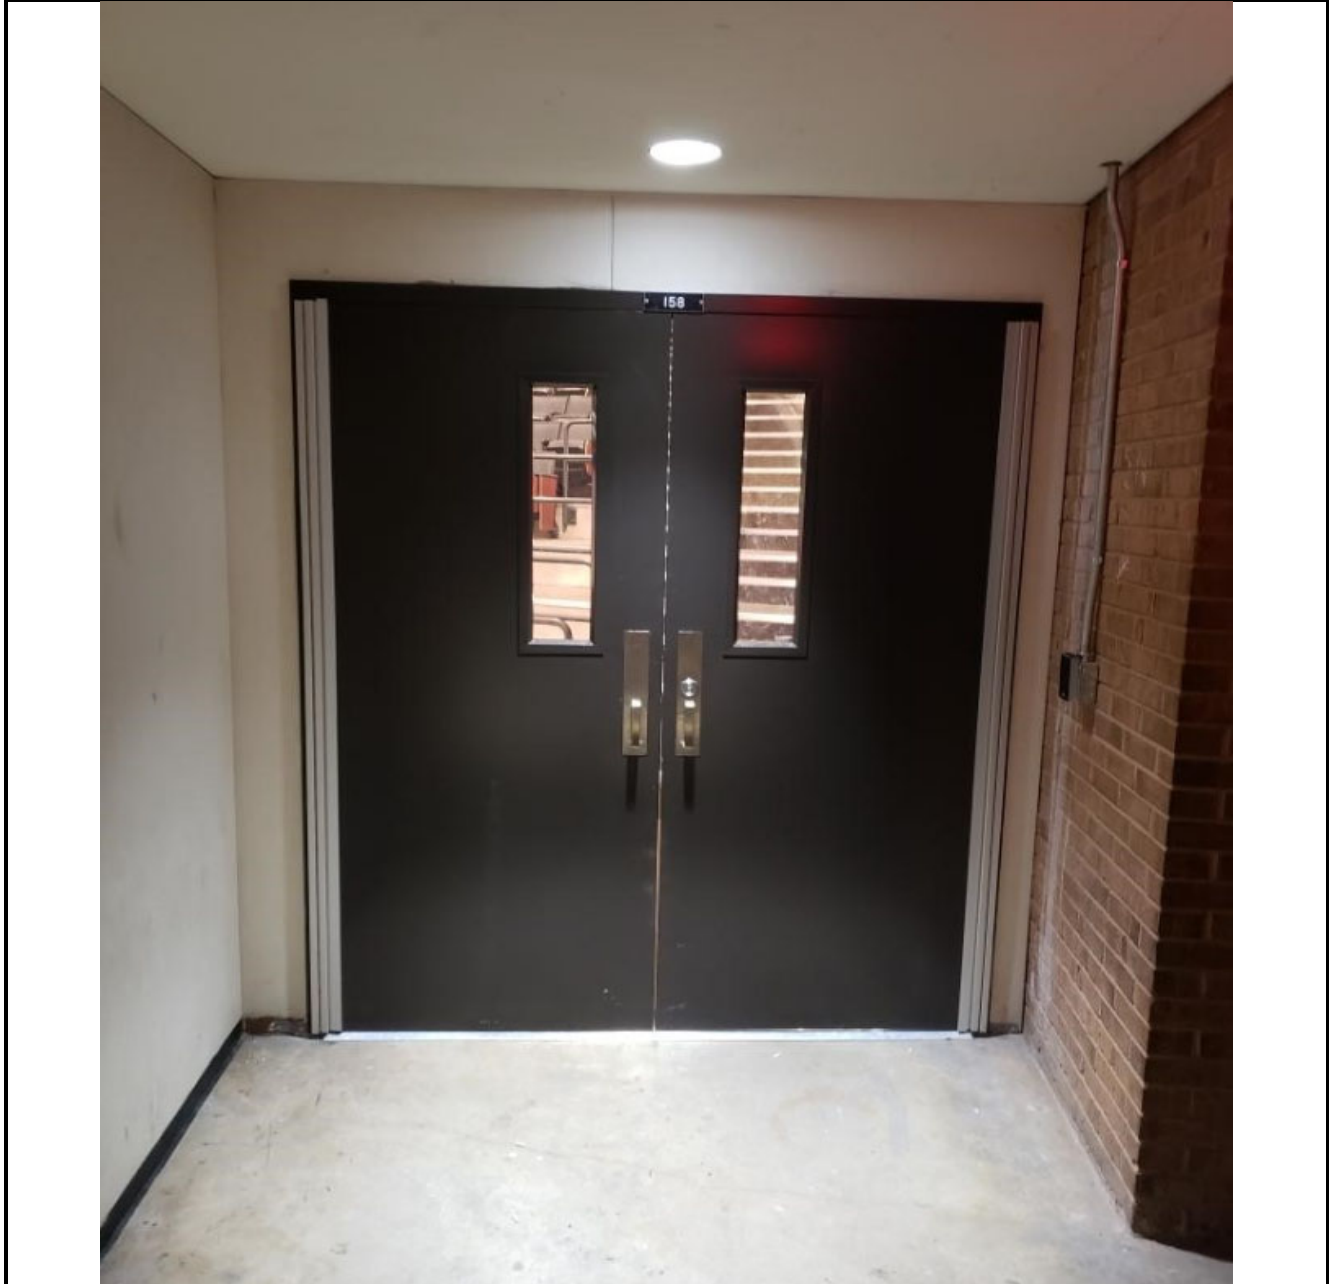

PROJECT INFORMATION	
PROJECT NAME: MATH SCIENCES ADD ACCESS CONTROL	DATE COMPLETED: JUNE 1, 2023
PROJECT NUMBER: 23012001	PROJECT MANAGER: SCOTT SUTO
NUMBER OF DOORS: 20	COST PER DOOR: \$8,200.34
PROJECT DESCRIPTION: ADDITION OF 20 DOORS OF ACCESS CONTROL AT THE MATH SCIENCES BUILDING. THE ENTRY DOORS TO ROOMS 108, 109, 121, 204, 260, 306, 336, 359, 360, 405, 406, AND 407 WERE RETROFITTED WITH DOOR CONTACTS, NEW ELECTRONIC MORTISE LOCKS OR LATCH RETRACTION KITS, ELECTRONIC TRANSFER HINGES, AND HID SIGNO CARD READERS. THE ALTERNATE ENTRY DOORS FOR ROOMS 121, 260, 306, 336, AND 406 WERE SETUP AS "TIME LOCK" DOORS AND RETROFITTED WITH DOOR CONTACTS, NEW ELECTRONIC MORTISE LOCKS OR LATCH RETRACTION KITS, AND ELECTRONIC TRANSFER HINGES. NEW LIFESAFETY POWER SUPPLY CABINETS ADDED IN TELECOM ROOMS 128, 222, 325, 353, AND 424. A NEW OPEN OPTIONS SSP CONTROLLER ADDED TO ROOM 128. OPEN OPTIONS RSC-2 SUB-CONTROLLERS ADDED TO THE EXISTING PANELS IN ROOMS 156 AND 246.	

PROJECT COST	
<b>DESIGN COST</b>	<b>\$ -</b>
ARCHITECT / ENGINEER / INTERIOR DESIGN	\$ -
<b>CONSTRUCTION COST</b>	<b>\$ 147,500.79</b>
DIVISION 1 - GENERAL REQUIREMENTS (DUMPSTERS, ETC.)	\$ -
DIVISION 2 - EXISTING CONDITIONS	\$ -
DIVISION 3 - CONCRETE	\$ -
DIVISION 4 - MASONRY	\$ -
DIVISION 5 - METALS	\$ -
DIVISION 6 - WOOD, PLASTICS & COMPOSITES	\$ -
DIVISION 7 - THERMAL & MOISTURE PROTECTION	\$ -
DIVISION 8 - OPENINGS	\$ -
DIVISION 9 - FINISHES	\$ -
DIVISION 10 - SPECIALTIES	\$ -
DIVISION 11 - EQUIPMENT	\$ -
DIVISION 12 - FURNISHINGS	\$ -
DIVISION 13 - SPECIAL CONSTRUCTION	\$ -
DIVISION 14 - CONVEYING EQUIPMENT	\$ -
DIVISION 21 - FIRE SUPPRESSION	\$ -
DIVISION 22 - PLUMBING	\$ -
DIVISION 23 - HVAC	\$ -
DIVISION 26 - ELECTRICAL	\$ 49,792.21
DIVISION 27 - COMMUNICATIONS	\$ -
DIVISION 28 - ELECTRONIC SAFETY & SECURITY	\$ 73,736.11
DIVISION 31 - EARTHWORK	\$ -
DIVISION 32 - EXTERIOR IMPROVEMENT	\$ -
DIVISION 33 - UTILITIES	\$ -
COMMISSIONING	\$ -
GENERAL LIABILITY	\$ -
GENERAL CONDITIONS (STAFFING, ETC.)	\$ 21,565.00
CONTRACTOR'S FEE (OVERHEAD & PROFIT)	\$ -
PAYMENT & PERFORMANCE BOND (NOT REQ'D IF UNDER \$100K)	\$ 2,407.47
<b>INFORMATION TECHNOLOGIES &amp; RESOURCES COST</b>	<b>\$ -</b>
UCF IT	\$ -
OFFICE OF INSTRUCTIONAL RESOURCES (OIR)	\$ -
<b>FACILITIES &amp; SAFETY COST</b>	<b>\$ 16,506.07</b>
BUILDING CODE OFFICE	\$ 2,776.00
STATE FIRE MARSHALL	\$ -
FP&C PROFESSIONAL MANAGEMENT SERVICES	\$ 13,275.07
FACILITIES OPERATIONS ALLOWANCE	\$ 455.00
CONSTRUCTION CONTINGENCY (10%, REFUNDED IF NOT USED)	\$ -
<b>TOTAL PROJECT COST</b>	<b>\$ 164,006.86</b>

PROJECT TIME		
START	PROJECT SUBMITTED BY CLIENT	1.75 MONTHS
	SPAA, F&S REVIEW	
	PM ASSIGNED	
	PM CONTACTS REQUESTER	
	PM DEVELOPS SCOPE	
DESIGN	A/E SELECTED	NA
	A/E PROPOSAL REVIEW	
	MPP TO CLIENT	
	CLIENT APPROVAL AND FUNDING	
	REQUISITION GENERATED	
	PO ISSUED (NOTICE TO PROCEED)	
	A/E DESIGN	
	WORKSHOPS	
	PERMIT REVIEWS	
BID/PERMIT	S/S PERMIT DRAWINGS REC'V'D	5.75 MONTHS
	PERMIT SUBMISSION	
	BUILDING CODE OFFICE REVIEW	
	STATE FIRE MARSHALL REVIEW	
	CONTRACTOR WALK-THROUGH	
	CONTRACTOR BID	
	PM REVIEWS BID	
	AVP F&S APPROVAL OF BID	
	PM PREPARES MPP	
	MPP TO CLIENT	
CONSTRUCTION	CLIENT APPROVAL AND FUNDING	1.5 MONTHS
	REQUISITION GENERATED	
	PO ISSUED (NOTICE TO PROCEED)	
	CONSTRUCTION STARTS	
	RFIS, SUBMITTALS, DOCUMENTS	
	PROGRESS REVIEWS	
	PAYMENT APPLICATIONS, INVOICES	
CLOSE-OUT	INSPECTIONS	0.5 MONTHS
	CERTIFICATE OF COMPLETION	
	CERTIFICATE OF OCCUPANCY	
	BENEFICIAL OCCUPANCY BY CLIENT	
	PUNCH LIST COMPLETION	
	FINAL INVOICES	
OWNER'S MANUALS	0.5 MONTHS	
ASSET TURNOVER TO OPERATIONS		
ACCOUNTING CLOSE-OUT		
<b>TOTAL PROJECT TIME - 9.5 MONTHS</b>		
