




PROJECT INFORMATION	
PROJECT NAME: CMB THIRD FLOOR ACCESS CONTROL	DATE COMPLETED: SEPTEMBER 25, 2024
PROJECT NUMBER: 24906003	PROJECT MANAGER: JOANNE TOOLE
NUMBER OF DOORS: 8	COST PER DOOR: \$8,404.05
PROJECT DESCRIPTION: THE MAIN ENTRY DOORS TO ROOMS 301K, 304, 303, 307, AND 308A RETROFITTED WITH DOOR CONTACTS, NEW ELECTRONIC MORTISE LOCKS, ELECTRONIC TRANSFER HINGES, AND HID SIGNO CARD READERS. THE ALTERNATE DOORS FOR ROOMS 303, 307, AND 308 SET UP AS "TIME LOCK" DOORS AND RETROFITTED WITH DOOR CONTACTS AND NEW ELECTRONIC MORTISE LOCKS, AND ELECTRONIC TRANSFER HINGES. DATA CABLING PROVIDED BY UCFIT. CLOSEOUT DELAYED BY APPROXIMATELY 2 MONTHS WAITING FOR UCFIT'S BILLING TO PROCESS.	

PROJECT IMAGES



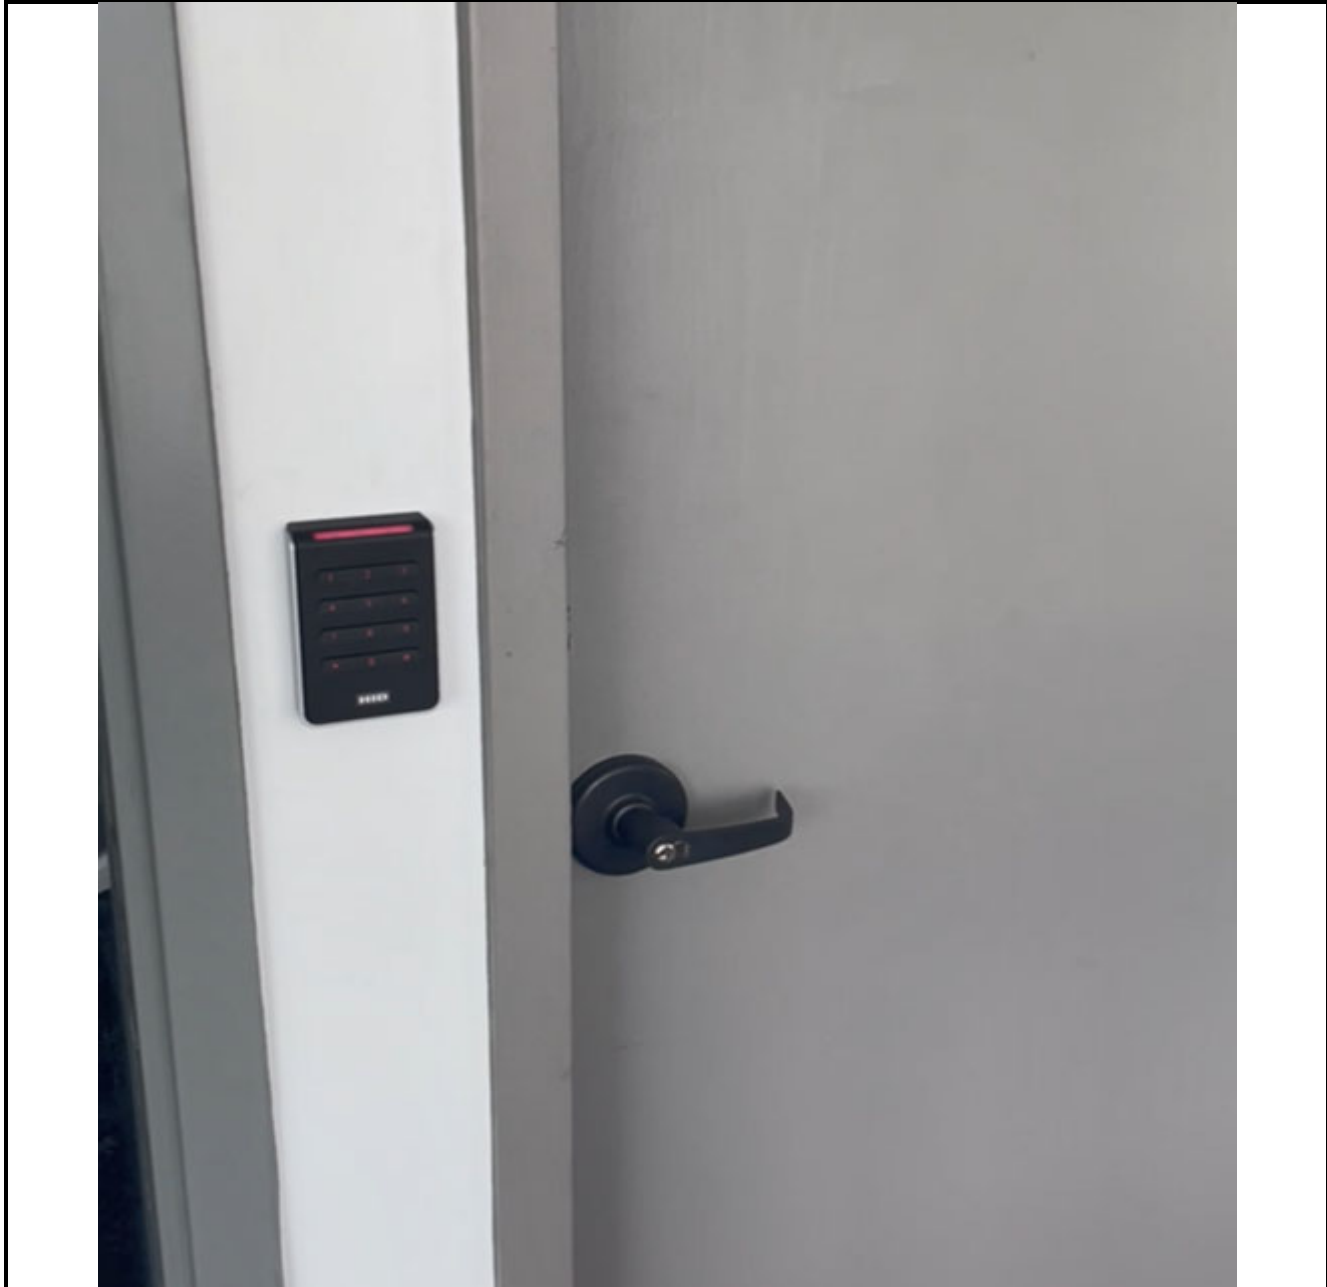

PROJECT INFORMATION	
PROJECT NAME: CMB THIRD FLOOR ACCESS CONTROL	DATE COMPLETED: SEPTEMBER 25, 2024
PROJECT NUMBER: 24906003	PROJECT MANAGER: JOANNE TOOLE
NUMBER OF DOORS: 8	COST PER DOOR: \$8,404.05
PROJECT DESCRIPTION: THE MAIN ENTRY DOORS TO ROOMS 301K, 304, 303, 307, AND 308A RETROFITTED WITH DOOR CONTACTS, NEW ELECTRONIC MORTISE LOCKS, ELECTRONIC TRANSFER HINGES, AND HID SIGNO CARD READERS. THE ALTERNATE DOORS FOR ROOMS 303, 307, AND 308 SET UP AS "TIME LOCK" DOORS AND RETROFITTED WITH DOOR CONTACTS AND NEW ELECTRONIC MORTISE LOCKS, AND ELECTRONIC TRANSFER HINGES. DATA CABLING PROVIDED BY UCFIT. CLOSEOUT DELAYED BY APPROXIMATELY 2 MONTHS WAITING FOR UCFIT'S BILLING TO PROCESS.	

PROJECT COST	
<b>DESIGN COST</b>	<b>\$ -</b>
ARCHITECT / ENGINEER / INTERIOR DESIGN	\$ -
<b>CONSTRUCTION COST</b>	<b>\$ 50,764.95</b>
DIVISION 1 - GENERAL REQUIREMENTS (DUMPSTERS, ETC.)	\$ -
DIVISION 2 - EXISTING CONDITIONS	\$ -
DIVISION 3 - CONCRETE	\$ -
DIVISION 4 - MASONRY	\$ -
DIVISION 5 - METALS	\$ -
DIVISION 6 - WOOD, PLASTICS & COMPOSITES	\$ -
DIVISION 7 - THERMAL & MOISTURE PROTECTION	\$ -
DIVISION 8 - OPENINGS	\$ -
DIVISION 9 - FINISHES	\$ -
DIVISION 10 - SPECIALTIES	\$ -
DIVISION 11 - EQUIPMENT	\$ -
DIVISION 12 - FURNISHINGS	\$ -
DIVISION 13 - SPECIAL CONSTRUCTION	\$ -
DIVISION 14 - CONVEYING EQUIPMENT	\$ -
DIVISION 21 - FIRE SUPPRESSION	\$ -
DIVISION 22 - PLUMBING	\$ -
DIVISION 23 - HVAC	\$ -
DIVISION 26 - ELECTRICAL	\$ -
DIVISION 27 - COMMUNICATIONS	\$ -
DIVISION 28 - ELECTRONIC SAFETY & SECURITY	\$ 50,764.95
DIVISION 31 - EARTHWORK	\$ -
DIVISION 32 - EXTERIOR IMPROVEMENT	\$ -
DIVISION 33 - UTILITIES	\$ -
COMMISSIONING	\$ -
GENERAL LIABILITY	\$ -
GENERAL CONDITIONS (STAFFING, ETC.)	\$ -
CONTRACTOR'S FEE (OVERHEAD & PROFIT)	\$ -
PAYMENT & PERFORMANCE BOND (NOT REQ'D IF UNDER \$100K)	\$ -
<b>INFORMATION TECHNOLOGIES &amp; RESOURCES COST</b>	<b>\$ 5,865.20</b>
UCF IT	\$ 5,865.20
OFFICE OF INSTRUCTIONAL RESOURCES (OIR)	\$ -
<b>FBO AND PERMITTING COST</b>	<b>\$ 7,692.48</b>
BUILDING CODE OFFICE	\$ 1,127.00
STATE FIRE MARSHALL	\$ -
PROJECT MANAGEMENT FEES	\$ 5,815.48
FACILITIES OPERATIONS ALLOWANCE	\$ 750.00
CONSTRUCTION CONTINGENCY (10%, REFUNDED IF NOT USED)	\$ -
<b>TOTAL PROJECT COST</b>	<b>\$ 64,322.63</b>

PROJECT TIME		
START	PROJECT SUBMITTED BY CLIENT	0.5 MONTHS
	SPAA, F&S REVIEW	
	PM ASSIGNED	
	PM CONTACTS REQUESTER	
	PM DEVELOPS SCOPE	
DESIGN	A/E SELECTED	NA
	A/E PROPOSAL REVIEW	
	MPP TO CLIENT	
	CLIENT APPROVAL AND FUNDING	
	REQUISITION GENERATED	
	PO ISSUED (NOTICE TO PROCEED)	
	A/E DESIGN	
	WORKSHOPS	
	PERMIT REVIEWS	
BID/PERMIT	S/S PERMIT DRAWINGS REC'D	1.5 MONTHS
	PERMIT SUBMISSION	
	BUILDING CODE OFFICE REVIEW	
	STATE FIRE MARSHALL REVIEW	
	CONTRACTOR WALK-THROUGH	
	CONTRACTOR BID	
	PM REVIEWS BID	
	AVP F&S APPROVAL OF BID	
	PM PREPARES MPP	
	MPP TO CLIENT	
	CLIENT APPROVAL AND FUNDING	
	REQUISITION GENERATED	
PO ISSUED (NOTICE TO PROCEED)		
CONSTRUCTION	CONSTRUCTION STARTS	1.75 MONTHS
	RFIS, SUBMITTALS, DOCUMENTS	
	PROGRESS REVIEWS	
	PAYMENT APPLICATIONS, INVOICES	
	INSPECTIONS	
	CERTIFICATE OF COMPLETION	
CLOSE-OUT	CERTIFICATE OF OCCUPANCY	3 MONTHS
	BENEFICIAL OCCUPANCY BY CLIENT	
	PUNCH LIST COMPLETION	
	FINAL INVOICES	
	OWNER'S MANUALS	
ASSET TURNOVER TO OPERATIONS		
ACCOUNTING CLOSE-OUT		
<b>TOTAL PROJECT TIME - 6.75 MONTHS</b>		
